


CONTENTS

Here is a short list of what we have been up to this season:

- 1. SHARP Trail Planning
- Lakes Basin Timber Work
- 3. Black Bear Run Construction
- 4. Sign Installation



SHARP Update

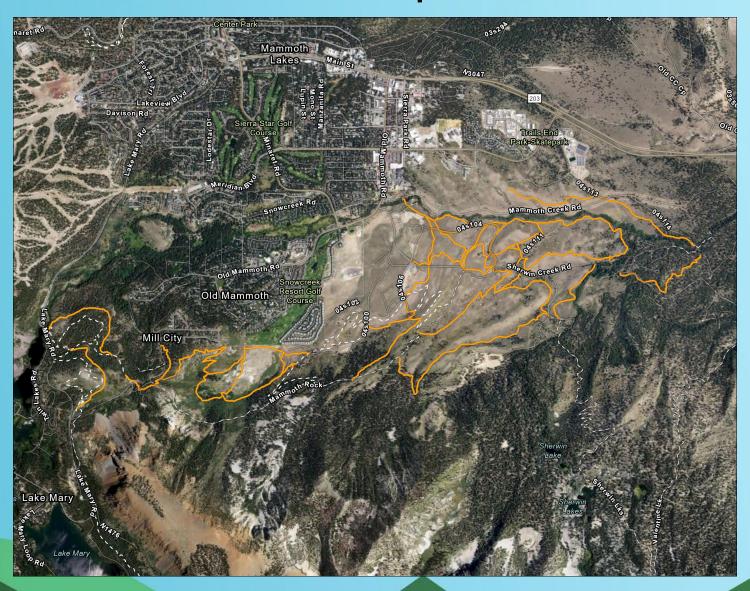

· Attendees:

- USFS Archaeology team
- USFS Tribal Relations
- USFS Recreation Officer
- USFS Wildlife Biologist
- USFS Hydrologist
- MLR SNC Grantee
- TOML Office of Outdoor Recreation

· Concerns:

- Archaeological Resources Avoid where possible. Shovel testing and monitoring or other mitigation practices where avoidance is impossible
- Hydrological concerns near Hidden Lake.
- Pine Marten Suitable habitat. Concerns about habitat fragmentation due to trail density.
- White Bark Pine.

Next Steps

- Recent Archaeological resource survey work completed by Stantec on behalf of TOML created comprehensive survey coverage of project area and was well received by USFS staff
- USFS to deliver resource avoidance dataset to TOML on 07/11
- TOML to redesign routes to avoid known resources where possible
- Interagency work to develop final vetted Proposed Action
- 11/16 tentative date for public meeting to discuss updated proposed action

Draft Timeline

Event	Calendar Days	Due Date
Project start date		06/01/24
Project Initiation (PIL, IDT ID, SUP Screening, etc)	21	06/22/24
Proposed Action Development (P+N, Internal scoping)	42	08/03/24
External Scoping / Public Involvement	42	09/14/24
Issue Identification	7	09/21/24
Effects Analysis Timeline Update ³	0	09/21/24
Required Regulatory Reports & Effects (specialists' input)	63	11/23/24
NEPA process check: is CE still appropriate?	0	11/23/24
Regulatory Concurrence (ESA, NHPA)	136	04/07/25
Decision Memo Prep	14	04/21/25
Sign Decision	0	04/21/25
Earliest Implementation ====>		04/21/25

Notes

FS constraints --> TOML vetted new alignments & draft proposed action --> FS review & publish PA


ESA Formal consultation for WBP (red fox) expected

Interdisciplinary Team Meeting 07/25

- All progress is waiting on the completion of Stantec Archaeological Impact Report
- USFS/TOML/Stantec met 07/31 to discuss next steps for completion of Archaeological Impact Report
- Updated draft timeline hovering around mid summer 2025 for earliest possible implementation date
- USFS voiced concerns around overall trail density

Interdisciplinary Team Meeting 07/25

Event	Vork Days	Due Date
Project start date ¹		06/01/24
Project Initiation (PIL, IDT ID, SUP Screening, etc)	15	06/22/24
Proposed Action Development (P+N, Internal scoping)	75	10/05/24
Exeternal Scoping / Public Involvement	30	11/16/24
Issue Identification	5	11/23/24
Effects Analysis Timeline Update ³	0	11/23/24
Required Regulatory Reports & Effects (specialists input) ⁴	45	01/25/25
NEPA process check - is CE still appropriate?	0	01/25/25
Regulatory Concurrence (ESA, NHPA)	90	05/31/25
Decision Memo Prep	10	06/14/25
Sign Decision	0	06/14/25
Earliest Implementation ====>		06/14/25

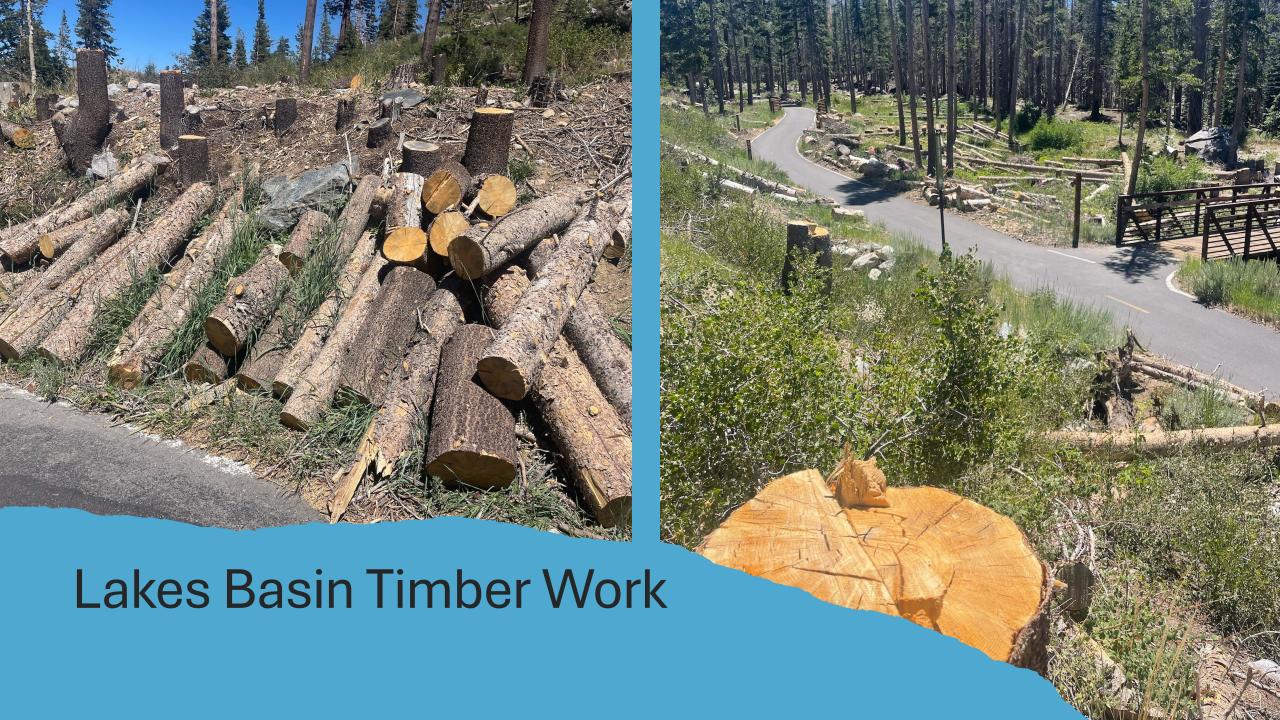



Lakes Basin Timber Work







Black Bear Run Construction Update





Black Bear Run Construction Update





Black Bear Run Construction Update

Sign Install – In Progress!



