Access Apartments Update

Presented by: Erik Guzman Project and Program Associate

November 4, 2024



1

Progress Photos

From 10/28/2024











Progress Photos From 11/01/2024









Construction Budget

- Change Orders: 7 Approved, 1 Pending
- Pay App: #3
- % Bid Increase: <1%
- % New Bid Spent: 15%

4 Access Apartments Update

Original Bid Amount Total Change	\$7,074,105
Orders	\$39,339
New Bid Total	\$7,113,444
% Bid Increase	0.56%
Total Pay App	\$1,053,602
New Bid Amount Left	\$6,059,843
0/ Now Did Croast	11010/

14 81%

% New Bid Spent

Development Budget

-	OG Budget (11/30/2023)	Actual Budget	Difference	<u>Percent</u> Change	Percent Spent to Date up to November 2024:
Land	\$1,255,374	\$1,255,374	\$0	0.00%	Development Budget
Rehab	\$6,990,871	\$7,074,105	-\$83,234	1.19%	
A&E + other soft	\$964,824	\$1,145,656	-\$180,832	18.74%	
Insurance + Taxes	\$187,500	\$231,822	-\$44,322	23.64%	
Permit + DIF	\$175,063	\$137,052	\$38,011	-21.71%	\$5,408,529
Reserves	\$60,000	\$60,000	\$0	0.00%	Total Budget \$ Spent-to-Date \$11,060,44
Contingency	\$740,432	\$740,432	\$0	0.00%	1
Developer Costs	\$416,000	\$416,000	\$0	0.00%	
TOTAL	\$10,790,064	\$11,060,441	-\$270,377	2.51%	
	Access Apartments Jpdate				

Project Update

Owner, Architect, Contractor (OAC) Meetings

 Weekly call to address issues, process change orders, identify topics for Board update, etc.

Financing

- CDBG / Town
- Mono County: Agreement signed waiting for check
- COC: Working with Inyo County legal Counsel
- Working with TOML to process predev reimbursement

Site Walk

 10/30 with Project Manager

Misc.

 Subs working extended hour to get dried in

Milestones

- Construction Start July 2024
- GC Contract expires June 2025
- Occupancy Fall 2025

Menemsha Construction 3 Week Look Ahead

	Menemsha Sierra Manor Housing											Tim M											
	SURVEY DESIGN					_]						Р	REPA	RED	DATE	 				11/1	/2024		
						⊢┤	<u>н </u>		3	We						,	\square	,		,			\uparrow
	I	Su	М	т	w	тн	F	Sa	Su					F		Su	M	Т	w	ТН	F	Sa	-
	DATE					11/7					11/12			-	5a 11/16			-			г 11/22		-
				11/5	1110		11/0	11/3			10/12	11/13	, 14	1113	11/10		1.710		11/20		11/22	11/23	
rt by 11/18	ON-SITE WORK																						
5	Building 'A']
	Roof Installation									?	?						х	Х	X	х	Х	Х	
& 2 nd floor)	HoldDowns Bolts		Х	Х	С																		
	Epoxy HoldDowns				С													ا		ر			
	Exterior Wrap-up		Х	х	X	x	С											ا		ا			
	Exterior Shear Inspection						C											<u> </u>		<u>ا </u>		<u> </u>	
floor by 11/20, &	Interior Framing 1st & 2nd Fl.		Х	Х	х	X	Х	Х		Х	С									<u> </u>			
-	Plumbing Rough In 1st Fl.									?	?	Х	Х	Х			х	Х	С				
	Plumbing Rough In 2nd Fl.													Х			Х	Х	X	Х	С		
	Window Prep.									Х	С												
	Exterior Doors									Х	Х	С								<u>ا</u>			
j	Windows Install									Х	Х	С	۱ <u> </u>					· ۱		۱ <u> </u>			
	Wrap Exterior												Х	X	Х								
	Building 'B'						1													<u>ا</u>			
eted by 11/12	2nd Fl. Steel & Bld. A Canopy		С															·		۱ <u> </u>			
	Roof Framing		Х	Х	х	х	Х	Х		Х	С												1
	Roof Nailing Inspection										С												
leted by 11/15	Exterior Doors											X	Х	С									
,	Roof Installation																?	?					
	Exterior Shear Inspection													С				<u> </u>		<u> </u>		[
leted by 11/20	Window Prep.			_	<u> </u>)						Х	C				<u> </u>					
	Window Install										\square						х	Х	С	<u> </u>			
					·۱													1		<u>ا</u>			


Updates

- Building A
 - Roof Installation Start by 11/18
 - Interior framing (1st & 2nd floor) completed by 11/12
 - Rough Plumbing 1st floor by 11/20, & 2nd floor by 11/22
 - Window Installed & Exterior Door by 11/13
- Building B

7

- Roof Framing completed by 11/12
- Exterior Doors completed by 11/15
- Window Install completed by 11/20
- Access Apartments Update

Funding Sources

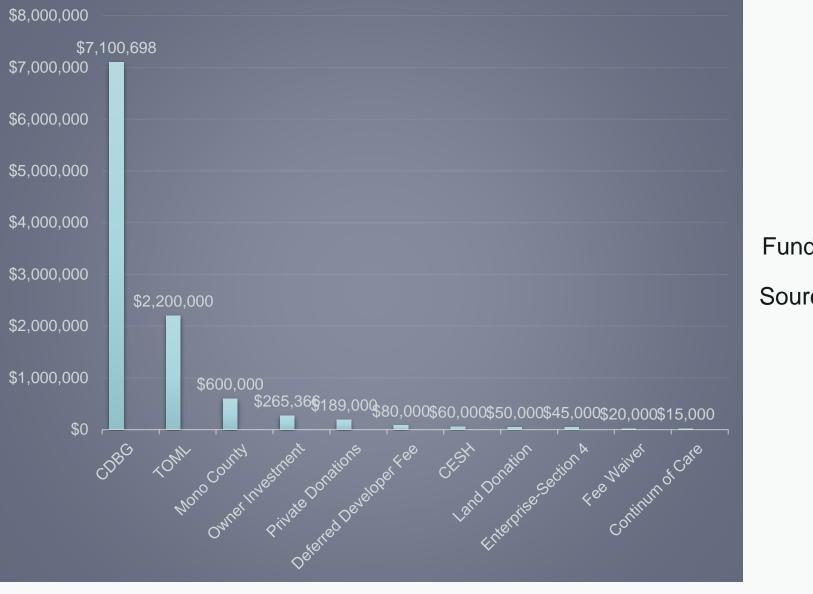

din g cce s	 CDBG \$7,100,698 TOML \$2,200,000 Mono County \$600,000 Owner Inv. \$265,366 Private Donations \$189,000 Def. Developer Fee CESH \$60,000 Land Donation \$50,000 Enterprise-Section 4 Fee Waiver \$20,000 Continuum of Care 	

8 Access Apartments Update

Background

2017

• Purchased by Mammoth Lakes Housing, Inc.

2018

• Request for Proposal (RFP) for architecture firm

2019

- Public design workshops
- NEPA environmental reports
- HOME Application submitted

2020

- Building permit approvals
- Cost of project increases by 39%

2021

- Value-engineering
- Fundraising launch
- CDBG application

2022

• NEPA update; secure construction financing; explore additional funding; meeting road show; pursue fee waivers; extend building permit; grant awards made, etc. HOME and CDBG grant awarded for more than \$6M.

2023

Final funding gap filled by Town of Mammoth Lakes and Mono County

Thank you

Erik Guzman (760) 934-4740 erik@eschousing.org
